Approved For Release 2004/05/21 : CIA-RDP80M00636A000100010047-9

24 May 1974

MEMORANDUM FOR THE RECORD

SUBJECT: Data Collection for Project KIQ

After examining the [redacted] STAT
and the [redacted] programs for CP/CMS, I have decide to
use [redacted] for inputting and collection of data for the
KIQ Project.

The size screen (564 characters) for the [redacted] was the STAT
primary disadvantage in the choice. Most of the data is
textual in content and is desirable to put 2000 to 3000
characters on the screen at one time.

[redacted] can process up to 3000 characters at a time and
the menu "language" is identical to that of the [redacted] -- STAT
very straight forward and easy to create.

It is anticipated that data collection will be done on
CP/CMS using the Delta Data 100 terminals.

[redacted] STA
KIQ Project Leader

Distribution:
Original - Project File
1 - [redacted] DCI/IC
1 - [redacted], C/CD/AD
1 - Chrono

Approved For Release 2004/05/21 : CIA-RDP80M00636A000100010047-9

Approved For Release 2004/05/21 : CIA-RDP80M00636A000100010047-9

KIQ SYSTEM FLOW CHART

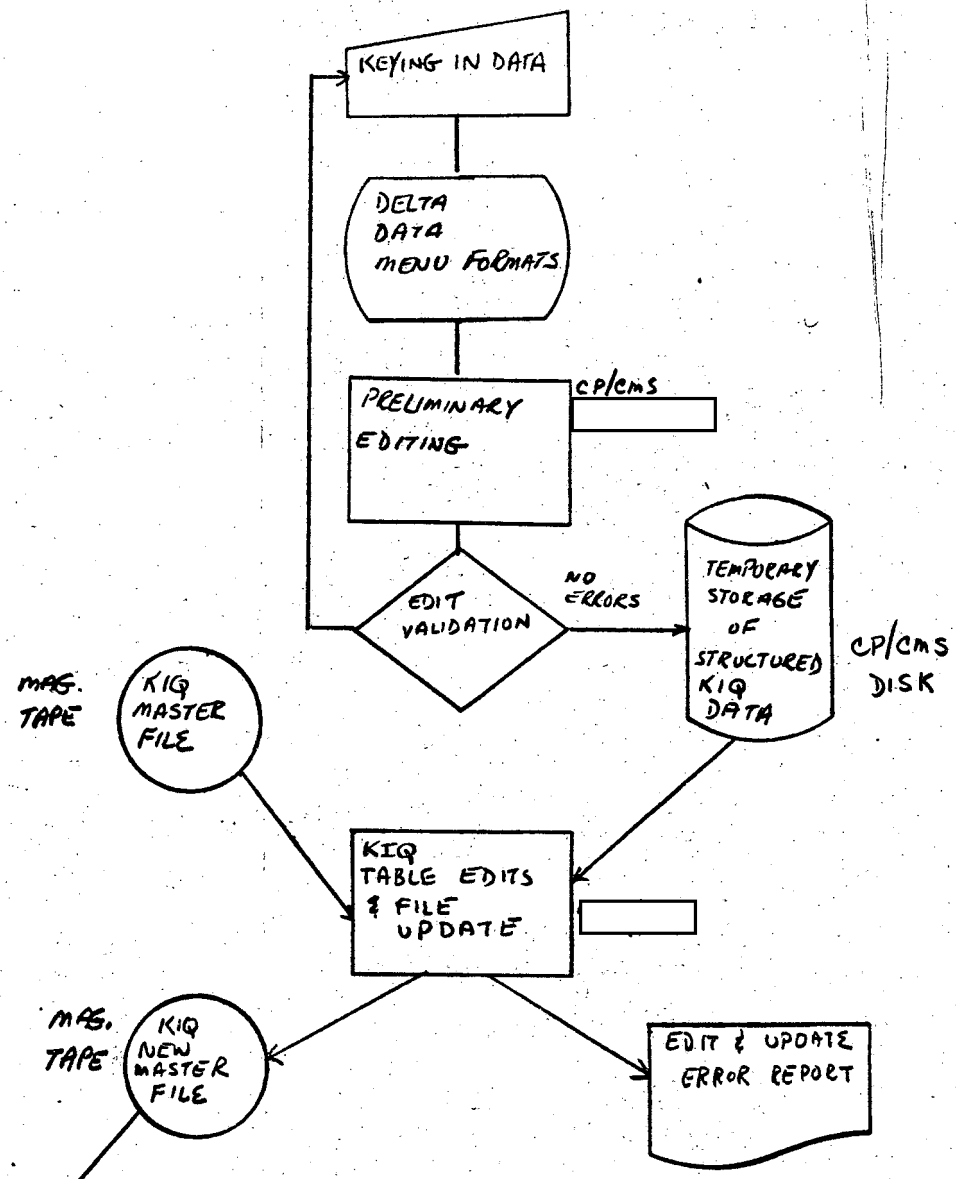

STAT

STAT

STAT

Approved For Release 2004/05/21 : CIA-RDP80M00636A000100010047-9

Approved For Release 2004/05/21 : CIA-RDP80M00636A000100010047-9

KIQ PROJECT MILESTONES

TASK DEFINITION	TARGET DATE	DATE COMPLETED
Project Proposal	20 Apr 74	20 Apr 74
System Design	30 Apr 74	30 Apr 74
Edit Specs	31 May 74	
Table Definition	6 Jun 74	
Menu formats (B)	28 May 74	28 May 74
Menu formats (P)	20 Jul 74	
Menu program (B)	6 Jun 74	
Menu program (P)	31 Jul 74	
Data Collection Structure	6 Jun 74	
Master File Update		
Code	13 Jun 74	
Debug	20 Jul 74	
Baseline Report		
Code	21 May 74	
Debug	30 Jun 74	
Performance Report		
Debug	21 Jul 74	
Crosstabs Reports	31 Aug 74	
USER Documentation	15 Aug 74	
USER Training	31 Aug 74	
System Testing	15 Sep 74	
Operational System	30 Sep 74	

(B) = Baseline
(P) = Performance

Approved For Release 2004/05/21 : CIA-RDP80M00636A000100010047-9
